

YELLOWSTONE CITY-COUNTY HEALTH DEPARTMENT
SUBSURFACE SEWAGE TREATMENT SYSTEM

PERMIT

DATE OF PERMIT 7/31/98

BUILDING PERMIT (A) B County #60-98
CLASS (1) 2
Y.C. PERMIT NO. 10568

SITE LOCATION 15916 Heather Lane

LEGAL DESCRIPTION C/S 2689 LOT BLK TRACT 52
Installer Montana Concrete
Installed For Mark Black

Type of Dwelling S.F. Constructed/designed for 3 Bdrms


WATER SUPPLY: Well X Cistern Public
Distance to septic tank 270' Distance to drainfield 280'

MINIMUM DRAINFIELD REQUIREMENTS: 190 Sq. Ft./Bdrm
Percolation Rate min./in. Depth of Groundwater Ft.

LAYOUT DETAILS:
Tank Size: 1000; 1500; 2000 gal. Material: Concrete X Other
Tank to Foundation: 18' Ft. Trench to property line Ft.

TRENCH DIMENSIONS:
Gravel above pipe 2" in. Gravel below pipe 6" in.
Depth to perf. pipe 22-26 in. Depth to bottom trench 32-36 in.
Trench width 24" System type standard

Total Area Installed: 700 sq. ft.

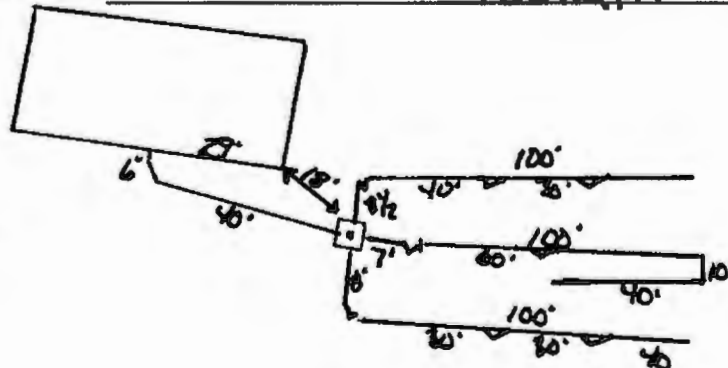

100
100
100
10
40
350 ft.
2
700 sq. ft.

APPROVED: X DENIED: REASON:
INSTALLER Harry Kagan SANITARIAN T. Lylander, R.S.

NOTE: Inspection denotes compliance to plans submitted and to Yellowstone County Rules and Regulations. It does not guarantee performance or longevity of system.
